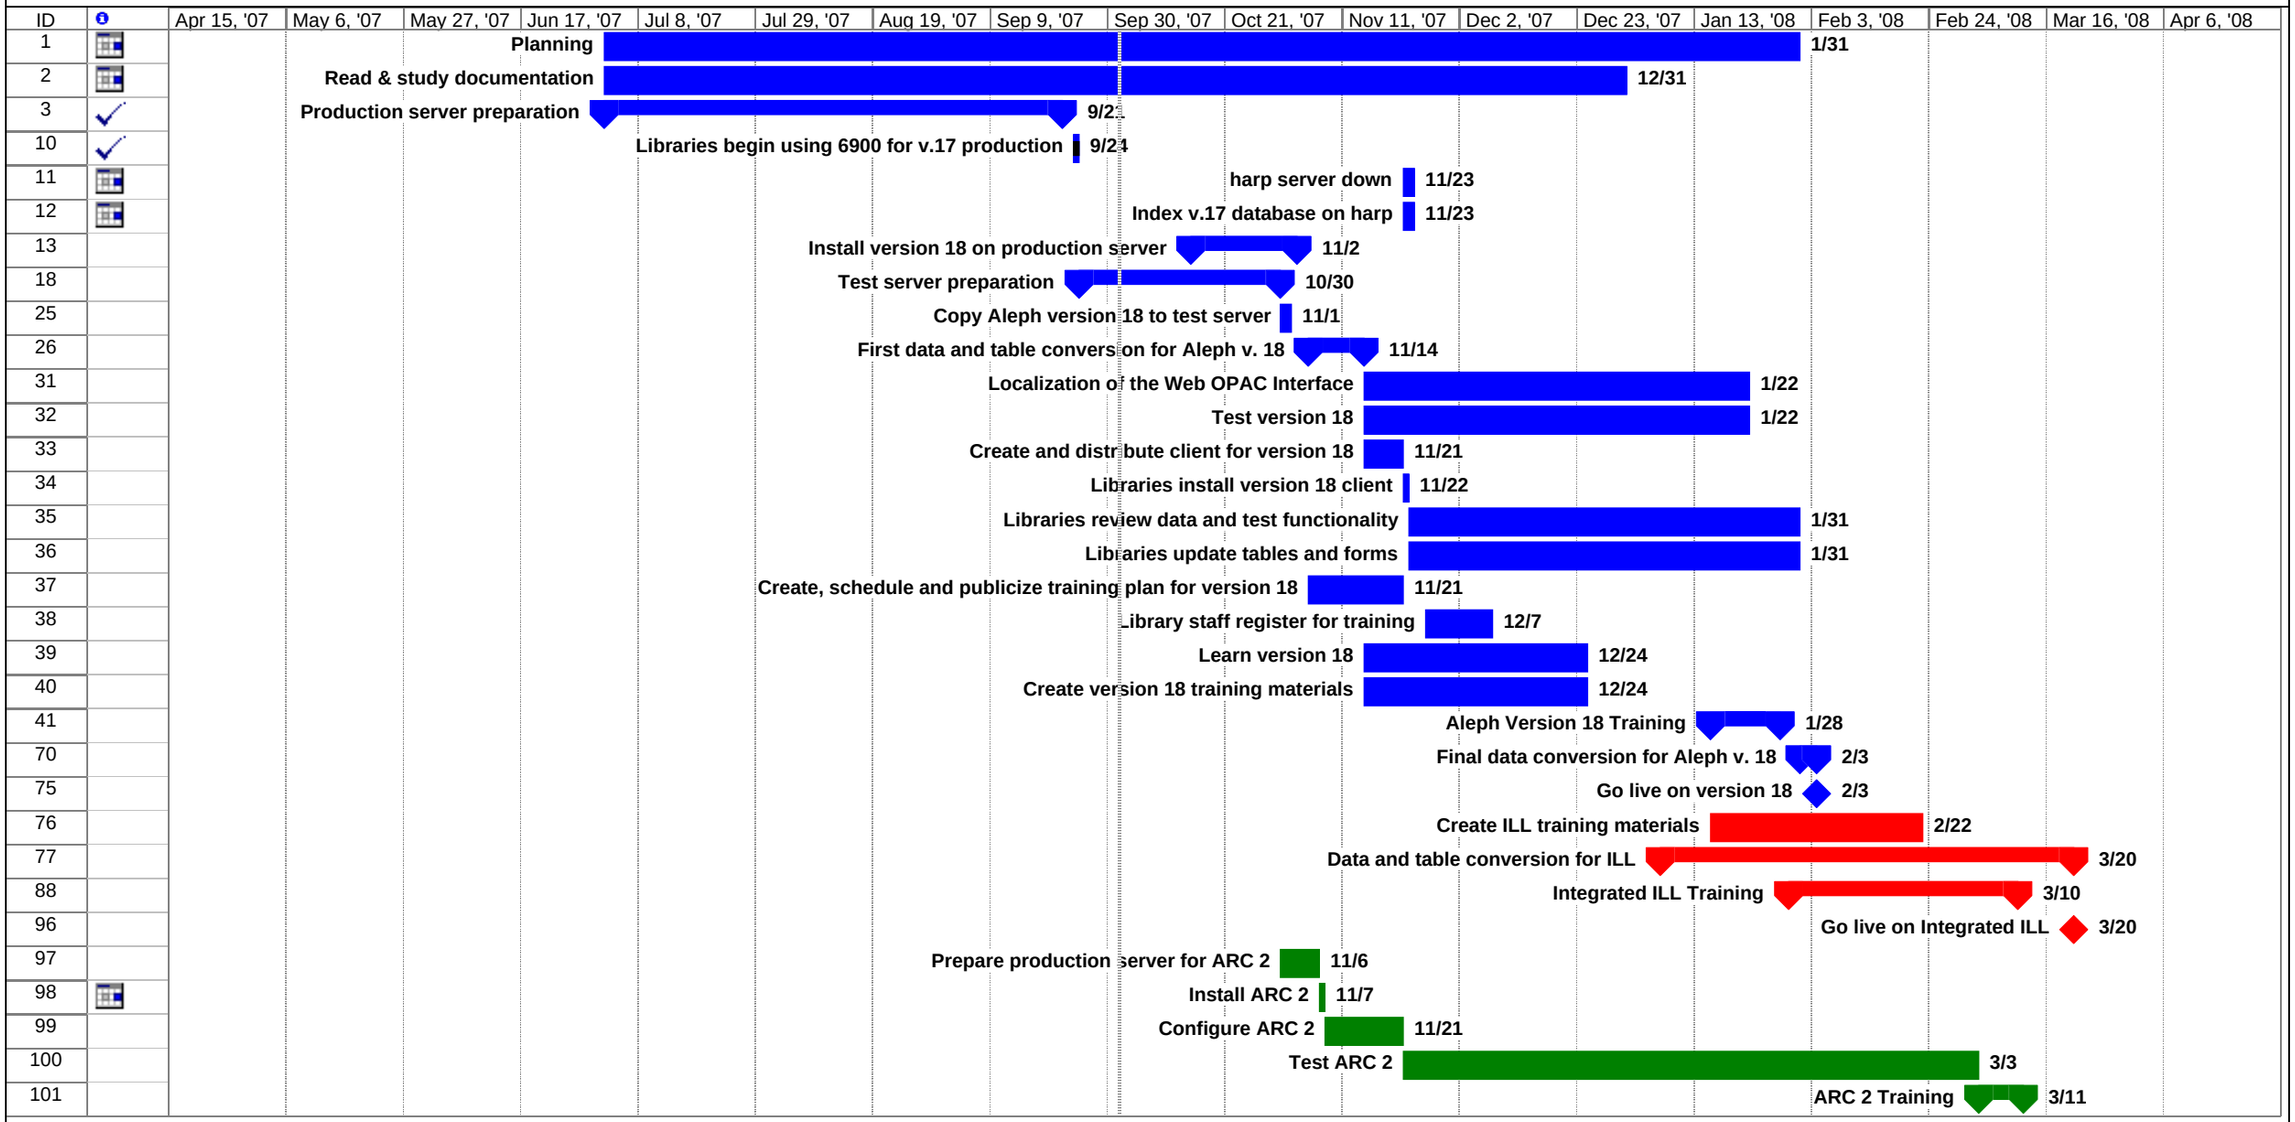
ID
Apr 15, '07
May 6, '07
May 27, '07
Jun 17, '07
Jul 8, '07
Jul 29, '07
Aug 19, '07
Sep 9, '07
Sep 30, '07
Oct 21, '07
Nov 11, '07
Dec 2, '07
Dec 23, '07
Jan 13, '08
Feb 3, '08
Feb 24, '08
Mar 16, '08
Apr 6, '08
1 Planning 1/31
2 Read & study documentation 12/31
3 Production server preparation 9/21
10 Libraries begin using 6900 for v.17 production 9/24
11 harp server down 11/23
12 Index v.17 database on harp 11/23
13 Install version 18 on production server 11/2
18 Test server preparation 10/30
25 Copy Aleph version 18 to test server 11/1
26 First data and table conversion for Aleph v. 18 11/14
31 Localization of the Web OPAC Interface 1/22
32 Test version 18 1/22
33 Create and distribute client for version 18 11/21
34 Libraries install version 18 client 11/22
35 Libraries review data and test functionality 1/31
36 Libraries update tables and forms 1/31
37 Create, schedule and publicize training plan for version 18 11/21
38 Library staff register for training 12/7
39 Learn version 18 12/24
40 Create version 18 training materials 12/24
41 Aleph Version 18 Training 1/28
70 Final data conversion for Aleph v. 18 2/3
75 Go live on version 18 2/3
76 Create ILL training materials 2/22
77 Data and table conversion for ILL 3/20
88 Integrated ILL Training 3/10
96 Go live on Integrated ILL 3/20
97 Prepare production server for ARC 2 11/6
98 Install ARC 2 11/7
99 Configure ARC 2 11/21
100 Test ARC 2 3/3
101 ARC 2 Training 3/11
